


Figure 1:
Hydro One Asset Modification/Relocation Process for Projects

Note: Proceed to Phase 1 only if asset modifications/relocations may be required.

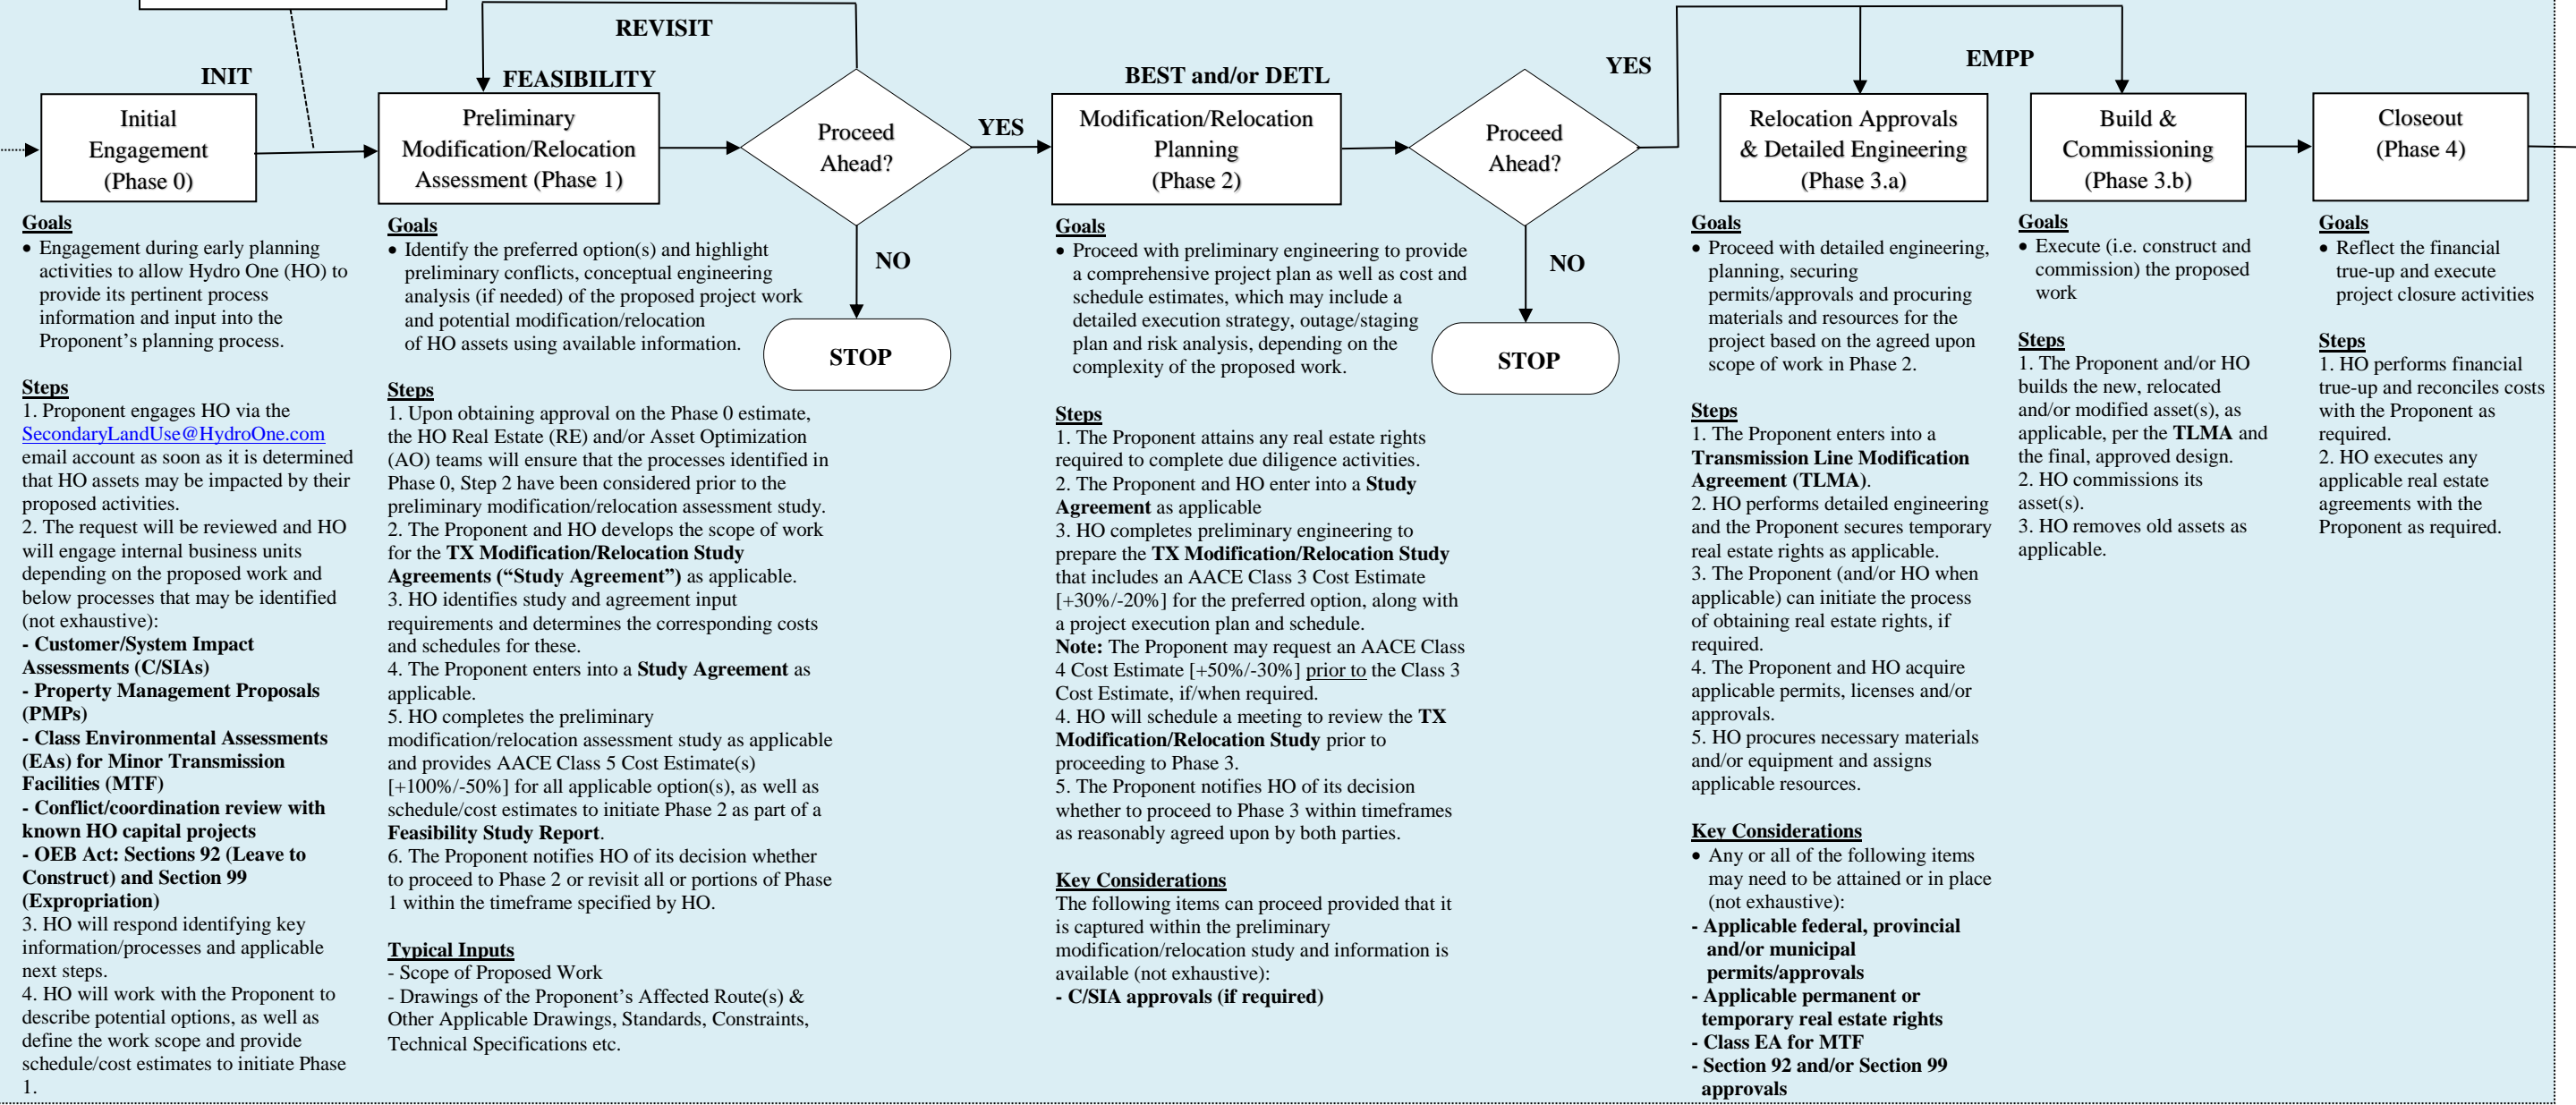

Phase Timeframes

	Simple Projects	Complex Projects
Phase 0	Varies based on the Scope & Complexity of the Proposed Work Activities	
Phase 1	3 - 6 Months	6 - 12 Months
Phase 2	3 - 9 Months	9 - 12 Months
Phase 3	6 - 12+ Months	12 - 24+ Months

Simple Projects: Straightforward OH or UG crossings impacting minimal assets (i.e. 1 - 2 structures); **Complex Projects:** Conflicts at multiple locations (i.e. parallel crossings, rail corridors) requiring elegant solutions

